



SIS Modernization Update

LSU Workday Student Website

www.lsu.edu/workdaystudent




Timeline & Accomplishments



LSU Cohort 1 Architect and Configuration (A&C) Stage Overview

A&C Stage

LSU Cohort 2 Stage Details

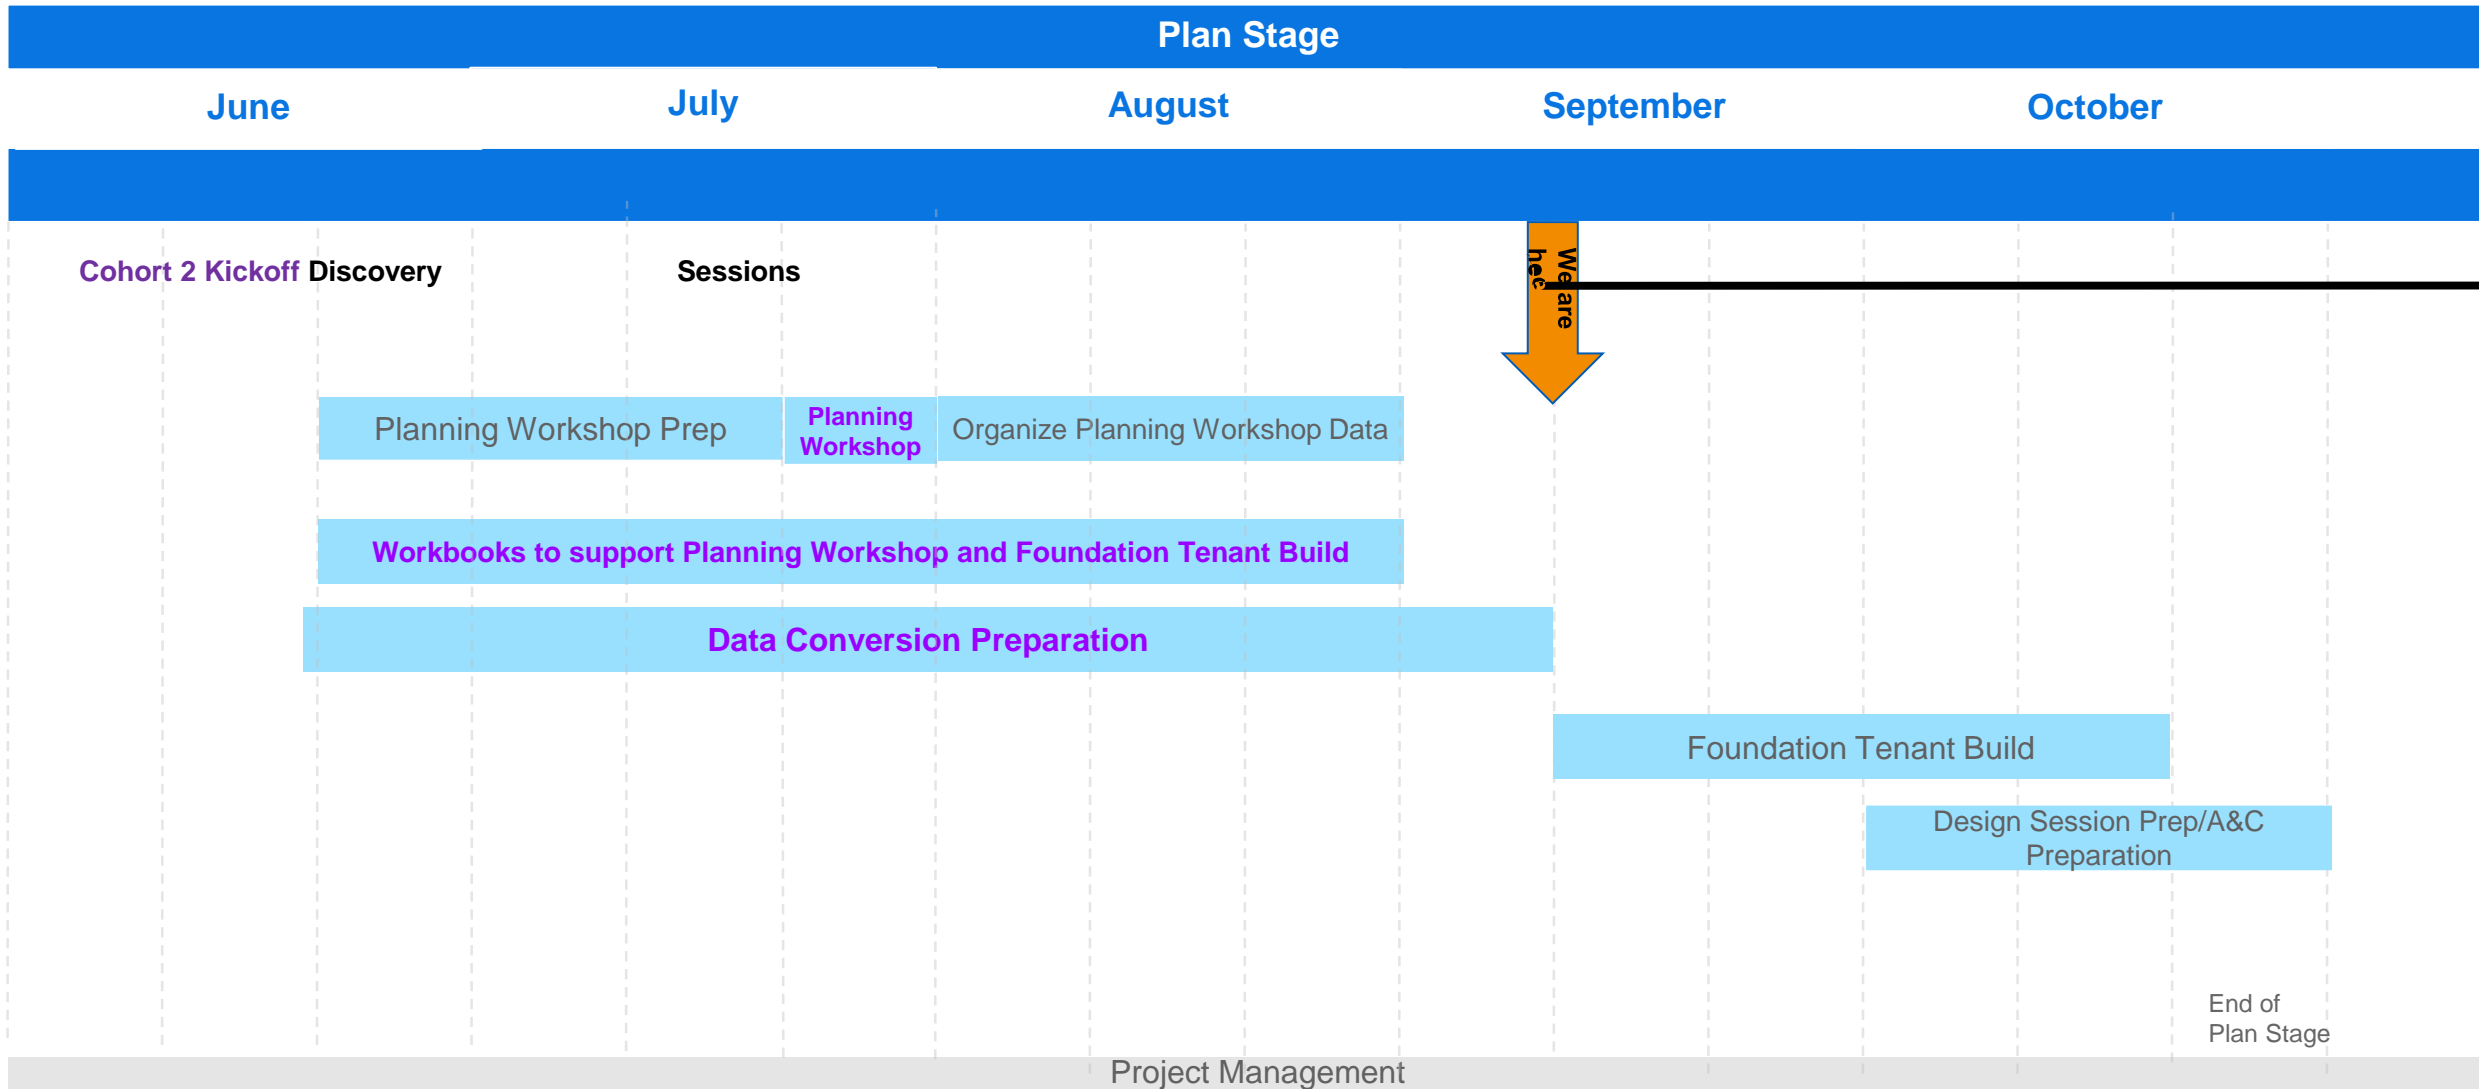

Key Accomplishments & Activities

as of 8/1/2023

Item	Due Date	Owner	Description/Update	Status
Cohort 2 Discovery Sessions	6/30/2023	Workday , LSU	Multiple sessions to validate current business processes	Complete
Cohort 2 Planning Workshop	7/27/2023	Workday , LSU	Onsite sessions to validate timeline, plan workset objectives, integrations and data conversions and review system of record	Complete
Training Phase III – Spring 2023	NA	LSU	Phase III Spring training underway	In progress
Cohort 1 Architect and Configuration (A&C) Workset B Objectives	8/31/2023	Workday , LSU	Completion of Workset Objectives, Data Conversion Programs and Integration Requirements identified for Workset B	In progress
Cohort 1 Workset B Tenant Planning and Build	9/29/2023	Workday	Build tenant based on Workset B Design and Configuration to be utilized for Workset C	In progress
Cohort 2 Foundation Tenant Planning and Build	10/13/2023	Workday	Build Cohort 2 Foundation Tenant to support Workset A Design and Configuration activities	In progress
Cohort 1 Workset C Tenant Validation	10/6/2023	Workday , LSU	Validate tenant build for Cohort 1 Workset C	Not Started

Key Training Dates

- **SEPTEMBER 2023**
 - Onboard Deloitte Training Developers
 - Begin to draft curriculum
- **MARCH 2024**
 - Finalize the Train-the-Trainer program and end-user training delivery
- **APRIL 2024**
 - Begin Train-the-trainer program(s)
 - End user training delivery begins
- **MAY 2024 – JANUARY 2025**
 - End user training delivery on-going
 - Development of training materials based on the on-going milestones

Student Program Update



Student Program Summary

as of 8/1/2023

Project

Projects with Resource Cross-over

as of 8/1/2023

EAB Navigate	TBD	LSUE	ITS	Going live in the Fall with currently planned functionality	100%	Complete	
Legacy System Decommissioning	Dec 2025	LSUAM	ITS	Replace and decommission legacy SIS	0%	Not Started	
Legacy System Decommissioning	TBD	LSUA	ITS	Replace and decommission legacy SIS	0%	Not Started	
Legacy System Decommissioning	TBD	LSUE	ITS	Replace and decommission legacy SIS	0%	Not Started	
Legacy System Decommissioning	TBD	LSUS	ITS	Replace and decommission legacy SIS	0%	Not Started	
